
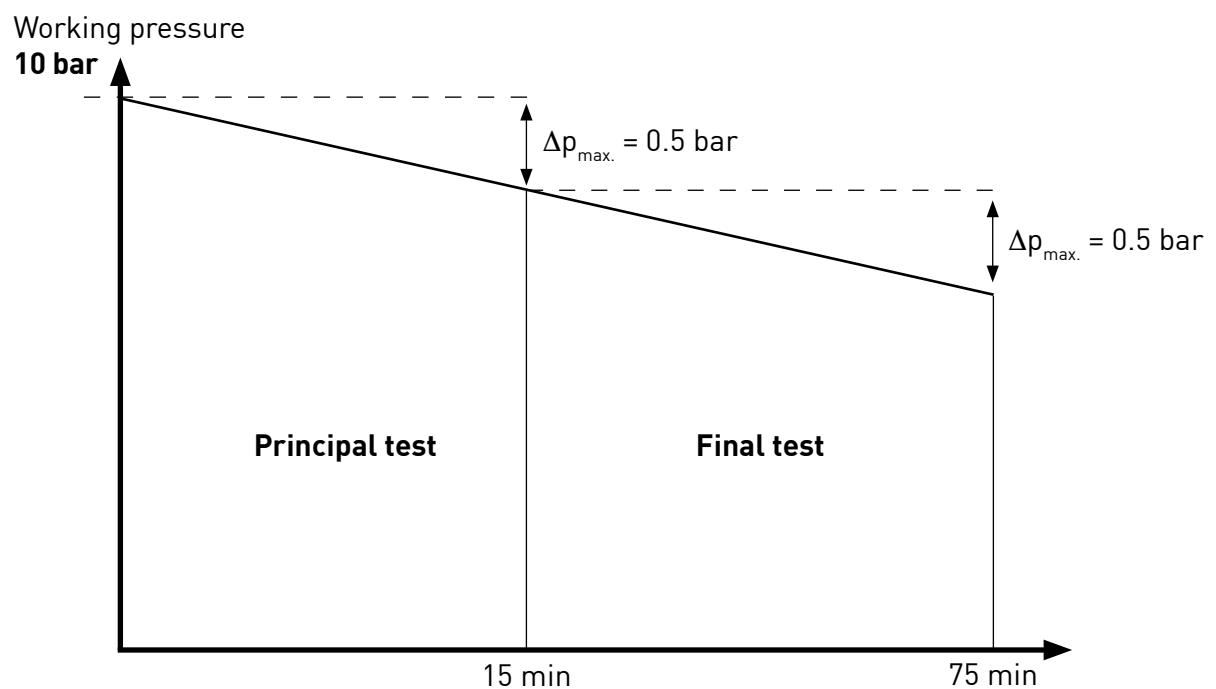


AQUATHERM RED

Sprinkler piping system

LEAKAGE TEST

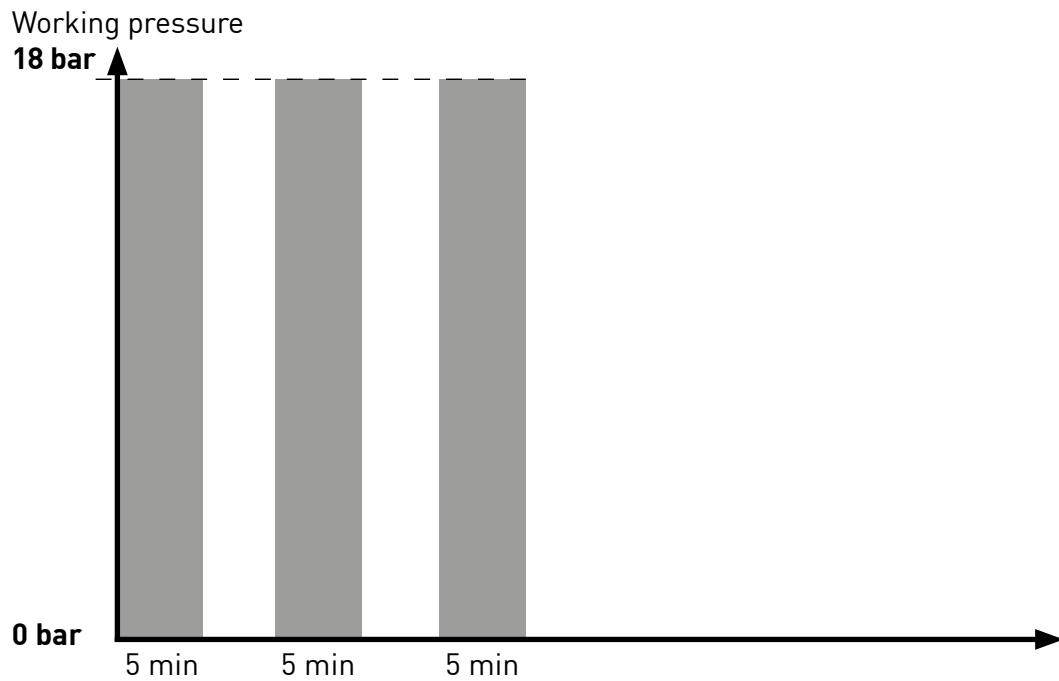

aquatherm GmbH

Technisches Büro

Biggen 5

D-57439 Attendorn

Place: _____

Object: _____

TEST RECORD AQUATHERM RED SYSTEM INSTALLATION

Note before the test: 3x 5 minutes system pressure of 18 bar for expansion/release of the pipes are required.

Preliminary test

The pipe system must be unpressurized between each cycle.

18 bar	5 min	realized:	yes ☐	no ☐
18 bar	5 min	realized:	yes ☐	no ☐
18 bar	5 min	realized:	yes ☐	no ☐

Principal test

Test pressure: _____ **10** bar

Pressure decline after 15 min: _____ bar **max. 0.5 bar**

Final test

(directly after the principal test, without changing the pressure)

Result principal test: _____ bar

Pressure decline after 60 min: _____ bar **max. 0.5 bar**

Notes:

Place, Date: _____

Please send the completed form to
info@aquatherm.de

Stamp/Signature

Client

Stamp/Signature

Contractor

AQUATHERM RED

Sprinkler piping system

aquatherm GmbH

Technisches Büro

Biggen 5

D-57439 Attendorn

Place: _____

Object: _____

DESCRIPTION OF INSTALLATION

Pipe length:

Ø 25 mm	_____	m
Ø 32 mm	_____	m
Ø 40 mm	_____	m
Ø 50 mm	_____	m
Ø 63 mm	_____	m
Ø 75 mm	_____	m
Ø 90 mm	_____	m
Ø 110 mm	_____	m
Ø 125 mm	_____	m
Ø 160 mm	_____	m

Start of test: _____

End of test: _____

Test period: _____

Test medium: ☐ water ☐ water/glycol

Client:

Contractor:

Place, Date: _____

Please send the completed form to
info@aquatherm.de

Stamp/Signature

Client

Stamp/Signature

Contractor
